



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Completed mass demolition
- Began installing temporary enclosures
- Installed temporary lighting
- Removed transite panels

GOALS NEXT 2 WEEKS:

- Continue selective demolition
- Start excavation

PHOTOS :

DATE: October 24, 2025

MRCC PROJECT PROGRESS:

PLAN

BUILD

INTERIOR

LAUNCH



MILESTONE CHECKLIST:

- ☒ Construction Start – 9/18/25
- ☐ Foundations Complete
- ☐ Steel Complete
- ☐ Enclosed
- ☐ MRCC Substantial Completion
- ☐ Playfield Completion



View of existing structure from Southeast

CONTINUED ON
NEXT PAGE >>>



DATE: October 24, 2025


MORE PROGRESS PHOTOS:



Mass demolition of addition



View of existing structure from Southwest

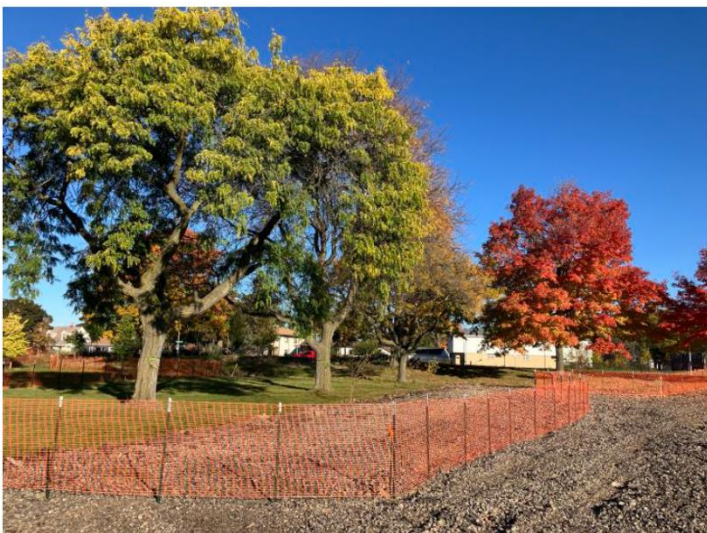

Tree protection fencing installed



Temporary lighting
