



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Interior trench block masonry complete at stepped footings.
- Masonry started Stairwell 4
- Concrete footings started Building C
- Surge tank concrete slab & walls poured

GOALS NEXT 2 WEEKS:

- Continue concrete foundation on building B
- Continue stairwell & load bearing CMU walls
- Continue concrete footings & foundation walls Building C


PROJECT HIGHLIGHT THIS WEEK:

- Surge tank slab & wall pours complete
- Footing excavation started Building C

Photos or Visual Assets:



Concrete foundation walls poured at Surge Tank

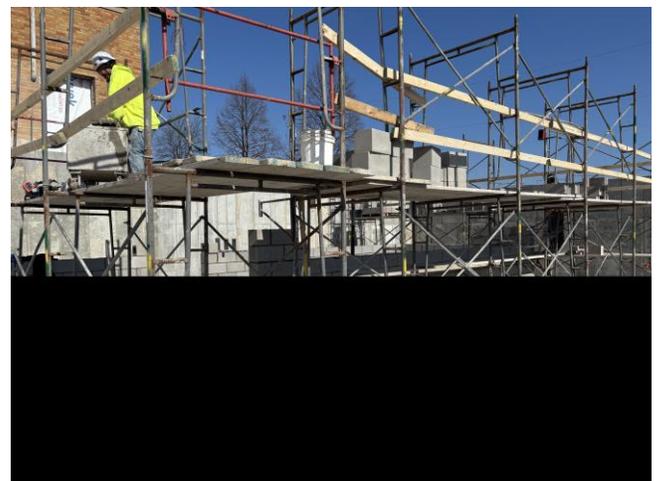

Stairwell 4 CMU Building B

DATE: February 13th, 2026

MRCC PROJECT PROGRESS:



MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion




Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

DATE: February 6, 2026


MORE PROGRESS PHOTOS:

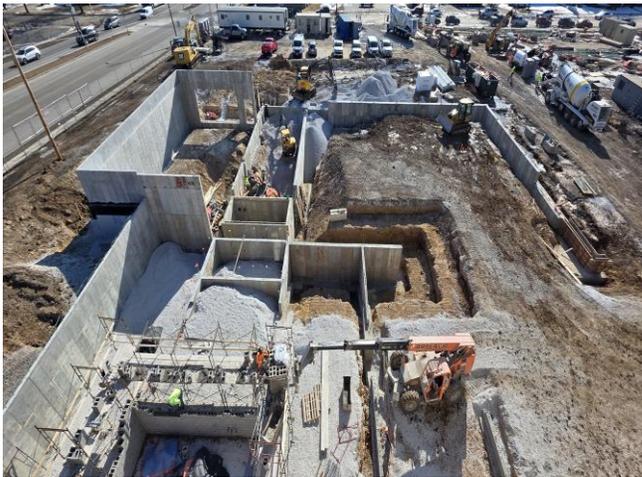

Aerial view of concrete foundations Building B



Concrete pump truck for surge tank foundation walls Building B

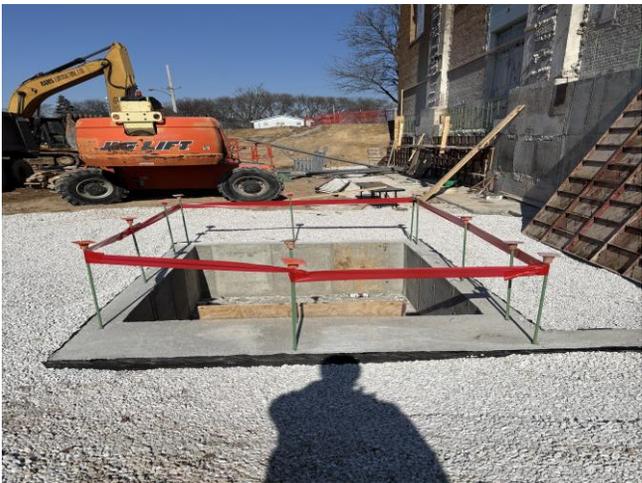

Elevator pit foundation Building C



Concrete footings Building C
