



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

PROGRESS THIS WEEK:

- Footings and foundation walls interior and exterior in area C
- Continue CMU load bearing interior CMU walls

GOALS NEXT 2 WEEKS:

- Continue concrete footings and foundations Area C
- Start precast bearing steel Area B
- Complete load bearing CMU walls for Area B precast

PROJECT HIGHLIGHT THIS WEEK:

- Superior completed pouring the last footings in area B1
- Construction bulletin one published

DATE: February 27, 2026

MRCC PROJECT PROGRESS:



MILESTONE CHECKLIST:

- Construction Start – 9/18/25
- Foundations Complete
- Steel Complete
- Enclosed
- MRCC Substantial Completion
- Playfield Completion

Photos or Visual Assets:



Interior foundation walls for surge tank.



Area B underground plumbing



Milwaukee Recreation Community Center & Browning Playfield

CONSTRUCTION UPDATE

DATE: February 27, 2026


MORE PROGRESS PHOTOS:



Area C Gymnasium



Footings and Column Pads Area C

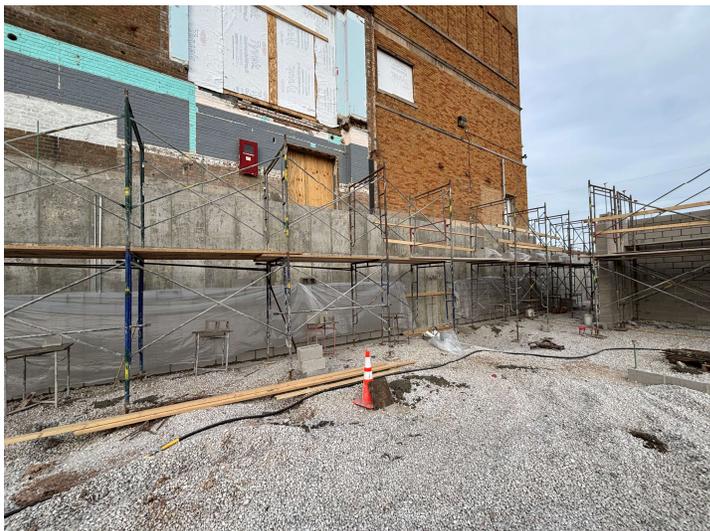

One-Side CMU Masonry Wall Area B



Building B under slab plumbing
